



Precinct 1 Transportation Task Force


March 28, 2013

PROJECT STATUS UPDATES

- FM 2181
- Lake Lewisville Bridge & FM 720
- FM 720 (North/South)
- FM 2499, Section 5
- FM 423
- US 377 Pilot Point
- US 377 Drainage Easements
- FM 455
- Mayhill Road
- IH-35E Ultimate
- Dallas North Tollway Extension

FM 2181

CSJ:	2054-02-015	2054-02-015	2054-02-016
Limits (From):	Lillian Miller	Lillian Miller	Corinth City Limits
(To):	IH-35E	Corinth City Limits	IH-35E
Jurisdiction:	Denton, Corinth	Denton	Corinth
Project Description:	Widen from two-lane to six-lane divided roadway		
Firm:	Huitt-Zollars	Key Contact:	David Nufer, Jeremy Doneghue
Schematic Approved:	December 15, 2005	Public Hearing:	November 2006
FONSI:	January 28, 2008	100% Plans E/W Section:	December 2012
ROW Acquisition Begins E/W Section:	November 2009	N/S Section:	January 2011
Utility Relocation E/W Section:	*	N/S Section:	*
DCIS Let Date E/W Section:	May 2013	N/S Section:	2017 (may be moved to an earlier date)

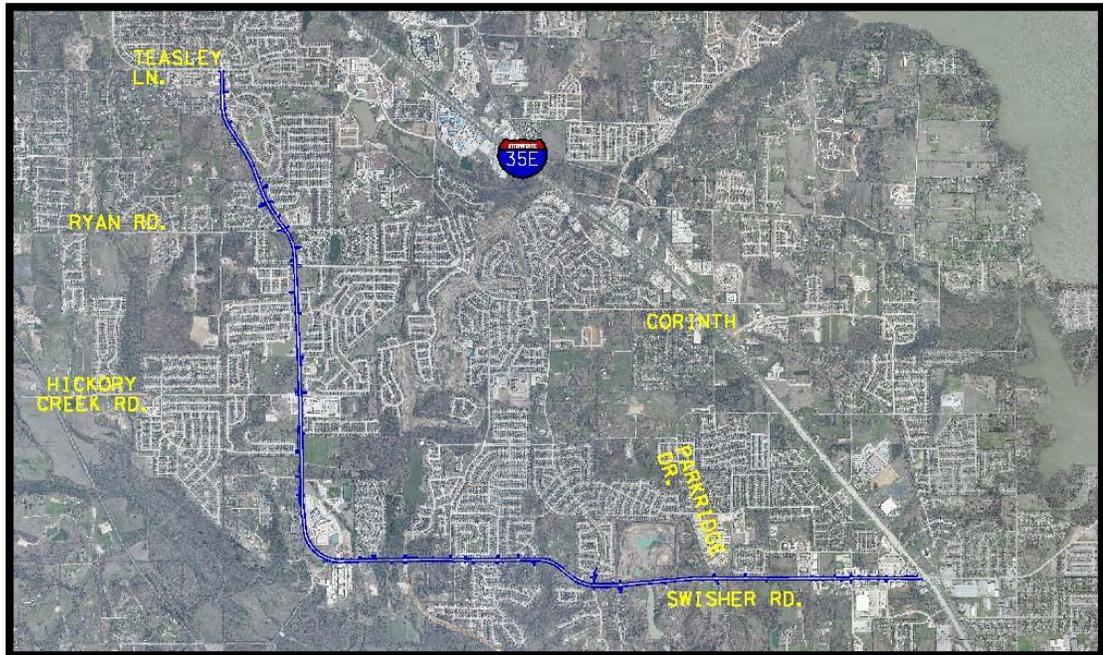

Current Activities:

- **ROW:** Acquisition is complete.
- **PS&E:** The project has been divided into two construction packages. The North/South Segment will consist of the construction from Lillian Miller to the City of Denton/Corinth City limits. The East/West Segment will extend from the City of Denton/Corinth city limits to IH-35E.
- **Funding:** Source not yet determined.
- **Utilities:** TxDOT contracted with Halff Associates to coordinate utility relocation.
- See attached utility coordination report from Halff Associates.
- TxDOT and ITS met with Upper Trinity on Friday, September 28, 2012, to discuss utility relocations.
- See attached project update report from Huitt-Zollars.

PROGRESS REPORT
FM 2181
DENTON COUNTY
March 2013

ROUTE STUDIES

Revised Schematic was approved by TxDOT on July 27, 2006.

Outstanding Issues: None

ENVIRONMENTAL ASSESSMENT

The FONSI was issued on January 28, 2008 and delivered to the TxDOT Denton area office the week of February 10, 2008.

Outstanding Issues: None

RIGHT OF WAY MAPPING

Outstanding Issues: Right of Way Appraisal Process.

ROW Acquisition is progressing well on the East-West Section and is essential complete.

ROW Acquisition is underway for the North-South Section of the Project.

Property 15 has been divided between two owners. ROW documents are being updated to reflect this change.

Parcel 37 has been updated to reflect the deletion of the ROW requirements.

Revised ROW takes along Summit Oaks subdivision to remove impact to sewer lift station and minimize impacts to subdivision HOA retaining wall. Parcels 21-30 have been revised to show no ROW takes.

Huitt-Zollars prepared and submitted revisions to ROW Parcel Documentation to address recent changes in ownership on several parcels.

Huitt-Zollars submitted documents to TxDOT for required drainage easements for both East-West and North-South Projects.

Huitt-Zollars is continuing to coordinate with TxDOT concerning the acquisition of drainage easements for the North-South project. Huitt-Zollars has provided design documentation verifying outfall requirements as requested by TxDOT to use in negotiations with various property owners and HOAs.

FIELD SURVEYING AND PHOTOGRAMMETRY

Outstanding Issues: Survey being scoped to tie FM2499 south project and FM2499 north project to FM2181 project. Huitt-Zollars has performed additional field survey to determine limits of temporary construction easements required to construct retaining wall at Summit Oaks Subdivision and screen wall at Corinthian Palisades Subdivision.

Additional survey was performed to account for recent developments along the corridor.

ROADWAY, DRAINAGE, SIGNING, MARKING, SIGNAL, AND TRAFFIC CONTROL DESIGN

Huitt-Zollars is preparing plans for a safety review meeting on the traffic control plans.

Huitt-Zollars submitted Final Hydraulic Report for the East West project and is preparing final document and is preparing the North – South Hydraulic Report.

Huitt-Zollars addressed final District Hydraulic Department comments and submitted final sealed Drainage Report to be forwarded to Austin for Division review.

Huitt-Zollars is completing all TxDOT forms required for PS&E submission packages to district and bridge section for completion of the plan review process.

Huitt-Zollars submitted 95% plans for the East-West Project to the District for their review on September 21.

Huitt-Zollars submitted a final sealed mylar PS&E package to District on February 13.

Huitt-Zollars addressed Austin Design Division comments on final sealed mylar set provided by the District.

Huitt-Zollars is continuing to prepare 95% PS&E plans for North-South Section of the project.

Huitt-Zollars is working with the TxDOT Denton Area Office to address median opening requests.

Huitt-Zollars provided electronic design files for the North-South Section in both .dgn and .dwg format for TxDOT's and City of Denton's use in utility relocation work.

Ongoing utility coordination meetings are being held with TxDOT, Lake Cities Municipal Utility Authority, Halff Associates, City of Denton, franchise utilities, and ITS to expedite the resolution of any PS&E challenges.

Huitt-Zollars has incorporated the connection at FM2499 into the FM2181 plans Develop wall plans and revise grading adjacent to Summit Oaks subdivision.

Huitt-Zollars is coordinating with Teague, Nall and Perkins to accommodate in the FM 2181 design plans improvements to Parkridge south of FM 2181.

Huitt-Zollars is coordinating with Brian Burke, P.E. to accommodate realignment of Crawford Road to be directly across from Oakmont Drive.

Huitt-Zollars has completed revising plans to accommodate a 14 ft outside lanes for shared use with bicyclist per recent federal policy statement on Bicycle and Pedestrian Accommodations Regulations and Recommendations as directed in TxDOT Memorandum dated March 23, 2011.

Huitt-Zollars has submitted Final signed Pavement Design Report to TxDOT

Huitt-Zollars met with TxDOT District staff on June 11th and presented final renderings/exhibit material to be used for public meeting to be held on June 19th with affected property owners.

TxDOT to schedule meeting with HOA for Summit Oaks subdivision to present exhibits/renderings of proposed noise wall/retaining wall.

Huitt-Zollars is continuing to coordinate with TxDOT and adjacent developments concerning the construction of screening walls. A public meeting was held on June 19th at TxDOT Denton County Area Office. Proposed wall options were presented to affected property owners in the Corinth Palisades subdivision and

TxDOT sent certified letters to all affected property owners in the Corinth Palisades subdivision requesting their vote on wall options. A majority picked an ashlar stone finish for the drop in precast panels. Huitt-Zollars has prepared 95% design plans and details for this wall which are included in PS&E package submitted to District on September 21st.

Outstanding Issues: Huitt-Zollars is working with Utility Coordinator (Halff Associates) on resolving utility conflicts. Utility conflict resolution for north-south section is currently in progress.
Huitt-Zollars received plans for Parkridge south improvements constructed by the City of Corinth. Huitt-Zollars is revising affected plan sheets to be forwarded on to TxDOT Design Division to be incorporated into sealed plan set.

Progress Report


TO: Denton County
FROM: Marc Epperly, P.E.
EMAIL: mepperly@halff.com
DATE: 3/27/2013
AVO: 26831 WO03
CSJ: 2054-02-016
Limits: From 866 ft. west of
Barrel Strap Rd. to IH
35
SUBJECT: FM 2181 (E-W) Progress Report

Utility Relocations

- **Atmos Energy** – Their plans and permit have been approved by TxDOT. The duration of their project should be about 60 days and their estimated completion date is May 31, 2013.
- **AT&T** – The relocations for their cell fiber are in progress and their estimated completion date is April, 10 2013.
- **Carrizo Gas** – We met with Carrizo on April 8, 2011 to discuss potential conflicts with their gas crossing west of Parkridge Dr. It was determined that their line is deep enough to clear construction and no relocations will be necessary.
- **Charter Communications** – They are mostly aerial on this project and will be relocating to Oncor Electric poles. Their TxDOT permit has been approved and their estimated completion date is April 30, 2013.
- **City of Corlntn (W&WW)** – The City's reimbursable agreement with TxDOT has been executed. The contract has been awarded and work has begun. Their estimated completion date is late April 2013.
- **CenturyLink** – They are currently working on their relocation design. We are coordinating with CenturyLink to complete their relocation plans. Their estimated completion date is July 2013.
- **Explorer Pipeline** – Explorer's reimbursable agreement package with TxDOT has been executed. Their relocations were completed in October 2012.
- **Grande Communications** – Grande's relocation plans and permit have been approved by TxDOT. Their estimated completion date is May 2013.
- **Lake Cities Municipal Utility Authority (LCMUA)** – LCMUA's reimbursable agreement package has been approved by TxDOT and their relocations are in progress. Their estimated completion date is May 2013.
- **Oncor Electric** – Oncor's reimbursable agreement with TxDOT has been executed and they have begun their relocation project. Their estimated completion date is April 2013.
- **Upper Trinity Regional Water District (UTRWD)** – UTRWD has submitted their reimbursable agreement package to TxDOT for approval. Their relocations will be part of the roadway construction contract.

LAKE LEWISVILLE BRIDGE & FM 720

CSJ:	1567-01-029
Limits (From):	Eldorado Parkway
(To):	FM 423
Ext. Const. Cost:	\$54,321,262.70
Description:	Construct a six-lane divided urban roadway from Eldorado Parkway to FM 423

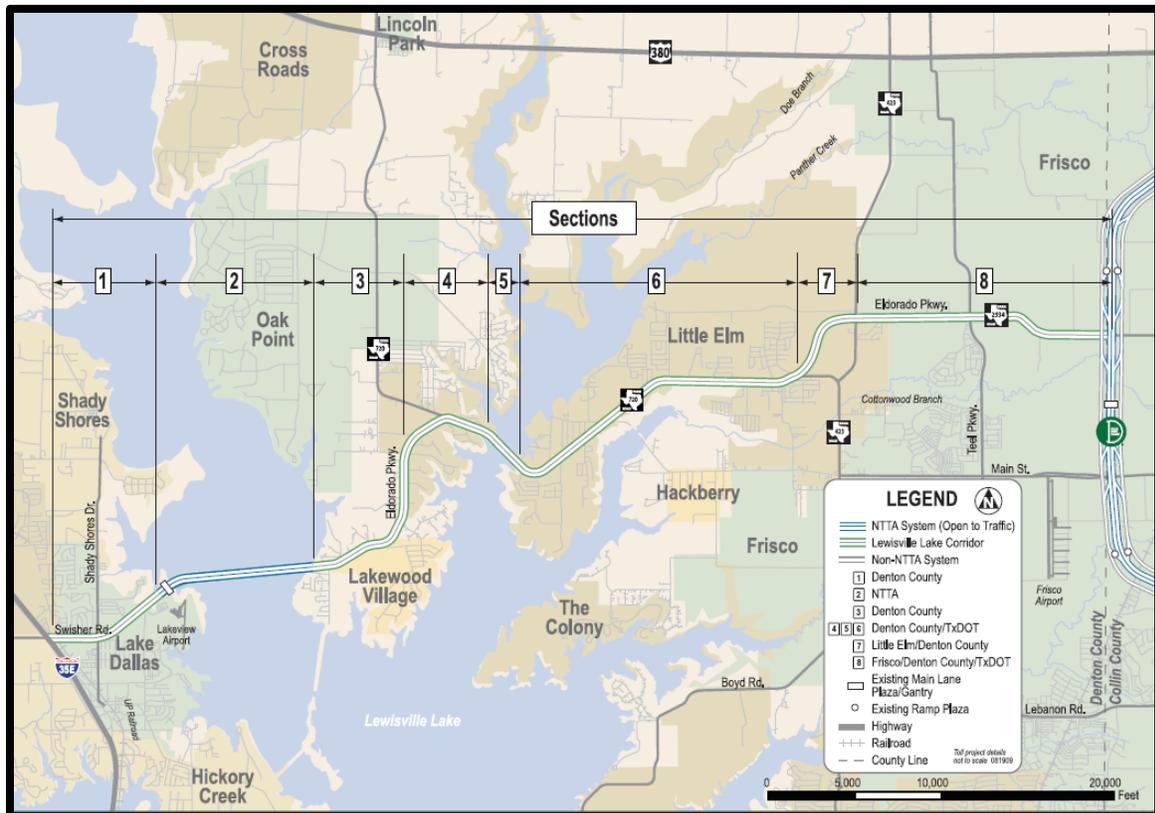

Current Activities

- **Construction:** FM 720 was let for construction in July 2010. The low bid was \$54,321,262.70, submitted by J.D. Abrams. There will be 566 contract days and 30 months of barricades.
- **See attached TxDOT Construction Report.**
- **Speed Study:** The Eldorado Speed Study is complete, and distribution has been made to Little Elm, Lake Dallas, Denton County, and NTTA. Lake Dallas has raised the speed limit to 45 mph between Shady Shores Drive and the bridge limits. NTTA has raised the speed limit on the bridge to 50 mph. Little Elm has also implemented a raised speed limit of 45 mph from Bay Ridge Drive to the bridge limits.

TxDOT Monthly Project Report for Precinct 1 Task Force

Date of report: March 26, 2013

Report prepared by: Tim Massey

Project: **STP 2010(982)MM, Etc.**

Control: **1567-01-029, Etc.**

Highway: **FM 720**

Limits: From: West of Garza Lane
To: West of FM 423

Contractor: **J.D. Abrams, L.P.**

TxDOT Project manager: Tim Massey
Contractor's Superintendent: Brian Barton

Phone: (972) 464-0426
Phone: (214) 688-0525

Date Work Began: July 14, 2011

Anticipated Completion Date: August 2014

Current Activities:

Current activities include: Phase 1 Lewisville Lake Bridge sidewalk and railing, approach slab, and concrete paving to enable traffic switch. Phase 1 substructure at Harts Branch Bridge. Phase 1 substructure at Peach Creek Bridge and retaining wall. Excavation, embankment, culvert installation, pipe installation, storm water treatment unit installation, inlets, SW3P, lime treated subgrade, retaining wall construction on FM 720. Asphalt and concrete pavement at west connector FM 720.

Narrative Description of last month's activities: Phase 1 Lewisville Lake Bridge, phase 1 substructure at Harts Branch Bridge, phase 1 substructure at Peach Creek Bridge, excavation, embankment, culvert installation, pipe installation, storm water treatment unit installation, inlets, SW3P, retaining wall construction. Asphalt and concrete pavement at FM 720 west connector.

Narrative Description of activities planned for next month: Removal of old Lake Lewisville Bridge. Harts Branch Bridge phase 1, Peach Creek Bridge phase 1, detours, pipe and culverts, retaining walls, excavation and embankment.

Traffic issues: None


Plans for changes in traffic patterns: Phasing of driveways and intersections. Traffic to be placed on newly constructed phase 1 portion of Lake Lewisville Bridge.

Item(s) of work currently controlling project completion: None

Other items of significance: Traffic to be placed on Lake Lewisville Bridge March 28.

FM 720 NORTH/SOUTH

CSJ:	1567-01-025	Complete Draft CE:	March 2006
Limits (From):	US 380	Schematic Approved:	October 2007
(To):	Garza Lane	Public Hearing:	August 25, 2011
Est. Const. Cost:	\$33,000,000	FONSI:	December 14, 2011
Project Description:	Widen two-lane rural roadway to six-lane divided urban	100% PS&E:	August 2013
		ROW Acquisition Complete:	September 2013
Firm:	TxDOT	Utility Relocation Begins:	September 2013
Key Contact:	Mike Hainline	Anticipated Let Date, South:	November 2013

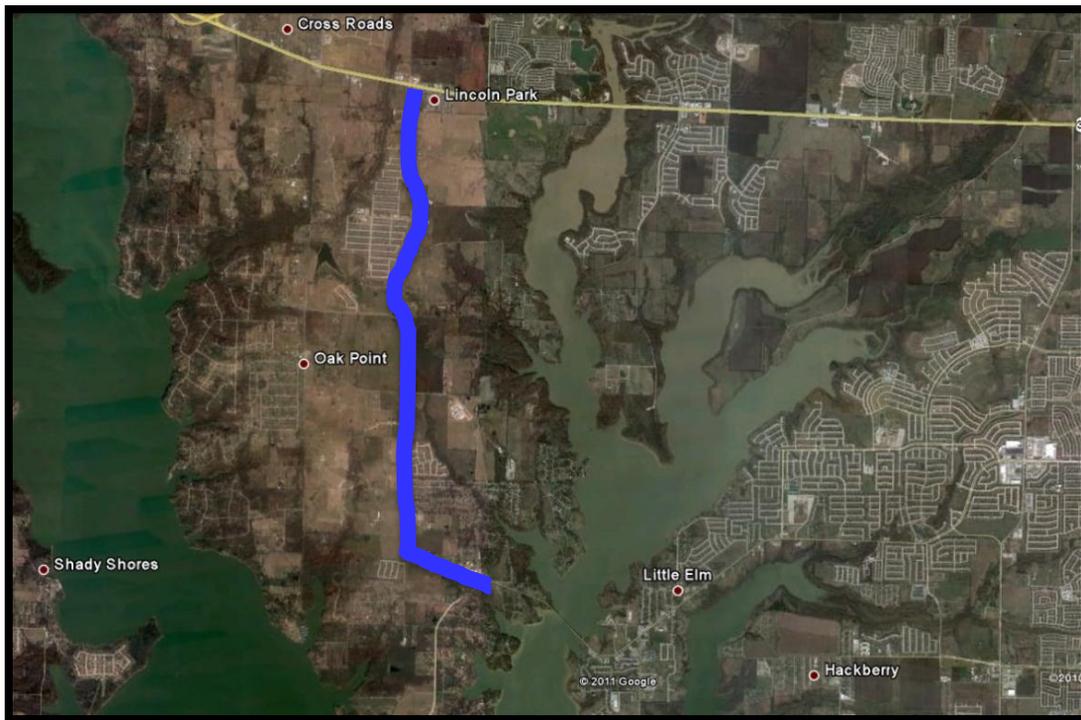

Current Activities:

- See attached TxDOT status report.
- **ROW:** ROW acquisition is approximately 34% complete.
- **Other:** ITS met with TxDOT to discuss this project on January 14, 2013.



FM 720: From Eldorado Pkwy to US 380 CSJ 1567-01-025 Denton County

PROJECT STATUS AS OF **Tuesday, April 02, 2013**:

COMPLETED MILESTONES

- Original Schematic Approved - [August 8, 2007](#)
- Completed 30% PS&E – [April 29, 2009](#)
- Original 60% PS&E Completed – [May 28, 2010](#)
- Revised Schematic approved – [November 4, 2010](#)
- Revised ROW Map approved: [March 21, 2011](#)
- Environmental Assessment approved: [July 5, 2011](#).
- Public Hearing: [August 25, 2011](#)
- Environmental Clearance: [December 14, 2011](#)
- **Revised 60% PS&E Completed – [March 20, 2013](#). 60% design plans given out at [March 20 utility coordination “kick-off” meeting](#). Plans to be uploaded to TxDOT FTP site ASAP.**

FUTURE MILESTONES

- **95% PS&E: est. [June 17, 2013](#) – submittal for TxDOT District internal review**
- **100% PS&E: est. [Aug 12, 2013](#) - submittal to TxDOT Austin office**
- **Letting Date: [November 2013](#)**
- **Construction start: est. [July 2014](#) as per a 6 month construction start delay to allow for utility relocations. Will review actual delay needed closer to project letting per “clear” dates provided by utility companies.**

DESIGN

- **PS&E: approx. 60% complete. Current design activity for 95% PS&E review submittal on [June 17, 2013](#):**
 - 1) **Process Retaining Wall layouts for review**
 - 2) **Finalize Traffic Control Plan, Stormwater Pollution Prevention Plan, Pavement Markings and Misc Roadway and Drainage Detail Sheets**
 - 3) **Permanent and Temporary Signal Design at Shahan/McCormick**
 - 4) **Finalize median openings per coordination with Area Office and cities**
 - 5) **Process regulatory speed limit change request for 45 mph to address safety concerns during construction**
 - 6) **Investigate Storm Water Treatment Unit alternatives at 2 locations**
 - 7) **Address 60% TxDOT internal review and city comments**
- **100% PS&E – estimate completion by [August 12, 2013](#).**

ROW

- ROW Mapping – Original ROW map completed [March 31, 2010](#). ROW Div accepted on [May 24, 2010](#).
- ROW Map revised and approved on [March 21, 2011](#). Revisions include: one parcel for parallel drainage, Schematic revision to avoid impacts to AT&T facility – Revise 7 parcels, remove 1 parcel (AT&T).
- Consultant working on ROW acquisition: PAS. TxDOT ROW PM: Lezlie Kirby. ROW appraisals and offers to property owners on-going. Monthly ROW status meetings held at the TxDOT District office.
- Request for Work Authorization to remove parcels noted below from the ROW map submitted on March 22.
Parcel 21E
Parcel 45 Parts 1 and 2
Parcel 48CE
Parcel 49 Part 2
- Estimate ROW acquisition south of Martop complete by [September 2013](#).

UTILITIES

- Subsurface Utility Engineering (SUE) provided by CardnoTBE to District on [July 29, 2010](#).
- Utility Coordination kick-off meeting held on [March 20, 2013](#). Next meeting on [April 18, 2013, 11:00 AM](#) at the Denton Area Office.
- Utility Relocations – Projected to begin by [September 2013](#) based on ROW acquisition time line.

SCHEMATIC AND ENVIRONMENTAL

- Revised schematic incorporating new alignment (avoid AT&T Central Office) approved on [November 4, 2010](#).
- Environmental Assessment (EA) approved: [July 5, 2011](#)
- Public Hearing: [August 25, 2011](#)
- Submitted public hearing packet for review: [November 16, 2011](#)
- Environmental Clearance Received: [December 14, 2011](#)

FM 2499, Section 5

CSJ:	2681-01-012
Limits (From):	FM 2181
(To):	IH-35E
Length:	2.97 miles
Est. Const. Cost:	\$31.8 million
Description:	Construct six-lane divided urban roadway
Firm:	Halff Associates
Key Contact:	Mike Romanowski
FONSI:	November 3, 2010
100% PS&E:	January 2012
ROW Complete:	*
Utilities Relocated:	*
Project Tracker Let Date:	May 2014
Construction complete:	*



Current Activity:

- **ENV:** This project will require non-regulatory mitigation and ongoing coordination. After approval of the EA, Halff will publish an NOA.
- **PS&E:** The 100% PS&E was submitted on January 9, 2012, for review.
- **Utilities:** Halff is currently working with the Area Office and utility owners to coordinate necessary relocations and has participated in twenty project-wide utility coordination meetings and several additional meetings requested by the various utility companies. The next project-wide utility coordination meeting will be held on April 18, 2013. See attached meeting minutes from the March 21, 2013, meeting.
- **ROW:** ROW and easement parcels have been reduced in size and deleted where possible with some minor design modifications. The total number of parcels has been reduced from 39 to 31.
- TxDOT has confirmed that RTR funds can be considered local funds. Denton County will still be required to contribute 10% of ROW costs, but will be given credit for ROW already purchased. The ROW LPAFA with TxDOT was executed by Denton County on May 1, 2012, and subsequently by TxDOT on May 10, 2012.
- There was a project kick-off meeting on October 30, 2012, to begin ROW acquisition. Appraisals have been completed. Offers have been made on 19 parcels.
- **Funding:** This project is fully funded with Regional Toll Revenue.
- **Let Date:** TxDOT has changed the project tracker date from May 2013 to July 2014. TxDOT has changed the project tracker date from July 2014 to May 2014.

FM 2499-5 Utility Coordination Meeting Minutes (03/21/2012)

Attendees:

- TxDOT: Danny Henderson; Tracy Beck; David Hensley
- Halff: Melanie Cleavelin; Josh Canuteson
- Others: Daniel Belser & Paul Pustejousky (DISD); Brent Keisman (COSERV); Fara Emadi & Don McLaughlin (DME)

Summary:

- I. INTRODUCTIONS
- II. PROJECT STATUS
 - a. Right of Way – No parcels closed yet but 2 just need a closing date and 7 others are close; 6 parcels in E.D. with a few more expected
 - b. Funding – RTR, Complete.
 - c. Letting Date – July 2014: DCIS now shows May 2014
- III. BASIC DESIGN INFO
 - a. Limits – From FM 2181 to IH 35E
 - b. Length – 2.919 miles or 15,440.39 ft.
 - c. Scope – Construction of a Non-Freeway Facility
- IV. UTILITY COORDINATION/QUESTION AND ANSWER
 - a. Utility Installation Review System
 - b. Utility Clearance Letters
 - c. Utility Agreements
 - d. Utility Companies
 - City of Denton: Phase 1 construction complete; Phase 2 design 80% complete
 - DISD: Same as last time; still needing 4 parcels; waiting to secure easements before starting design
 - COSERV Gas: Same as last time; waiting for ROW agreement with State School for Phase 2.
 - DME: Still resolving switch gear issue at Pine Hills; have about 10% design
 - Level 3: Working on design
- VI. NEXT STEPS
 - a. Plan Distribution
 - b. Data Collection
 - c. Future Meetings April 18, 2013

FM 423: NORTH & MIDDLE

CSJ:	1315-02-009
Limits (From):	Stewart Creek Road
(To):	US 380
Length:	6.91 miles
Ext. Const. Cost:	To be determined
Description:	Construct four- to six-lane divided urban roadway
Firm:	Jacobs Engineering
Key Contacts:	Debbie Neubert
ROW Acquisition Began:	December 2010
ROW Acquisition Complete:	July 2012
Utility Relocation Began:	July 2011
Utility Relocation Complete:	August 2013
Let Date:	September 2013
Construction Begins:	December 2013
Construction Complete:	May 2016



Current Activity:

- **ROW:** ROW acquisition is complete.
- **PS&E:** 100% Plans have been completed.
- TxDOT shows the project let date to be September 2013; however, the project may be eligible to let at an earlier date.
- **See attached Jacobs Progress Report.**
- **See attached TxDOT Project Report.**

- I. Efforts this month:**
 - Addressed final comments from TxDOT on the Illumination plans
- II. Right-of-Way Acquisition efforts this month for the North Section**
 - ROW acquisition complete: 63 parcels closed out of 63 total parcels.
- III. Utility Coordination Effort for the north section:**
 - The TxDOT Denton Area Office has taken over responsibility for the utility coordination.

TxDOT Monthly Project Report for Precinct 1 Task Force

Date of report: March 26, 2013

Report prepared by: Noe Rodriguez

Project: **C 1567-2-27**

Control: **1567-02-027**

Highway: **FM 423**

Limits: From: 0.6 miles south of FM 2934 (Eldorado Parkway)

To: Stewarts Creek Road

Contractor: **Austin Bridge & Road, LP**

TxDOT Project manager: Noe Rodriguez

Phone: (214) 923-2242

Contractor's Superintendent: Steve Gould

Phone: (214) 596-7300

Date Work Began: December 10, 2009

Anticipated Completion Date: May 2013

Current Activities: 7-11 and Aspen change orders

Narrative Description of last month's activities: 7-11 and Aspen change orders

Narrative Description of activities planned for next month: Place 7-11 driveway & Aspen sidewalk and ramps.

Traffic issues: None


Plans for changes in traffic patterns: n/a

Item(s) of work currently controlling project completion: 7-11 driveway, Aspen slopes, sidewalk, and ramps.

Other items of significance: 7-11 driveway, Aspen slopes

US 377 PILOT POINT

CSJ:	0081-06-029	Begin Advanced Planning:	June 2010
Limits (From):	Grayson County Line	Complete Draft Env. Document:	August 2011
(To):	North of N. Washington Street	Schematic Submitted:	September 2011
Est. Const. Cost:	\$12 million	Public Hearing:	July 27, 2010
Project Description:	Reconstruction of roadway to include a continuous left-turn lane	Environmental Clearance:	August 30, 2012
Length:	3.5 miles	100% Plans	April 2013
Firm:	Bridgefarmer	ROW Acquisition Begins:	*
Key Contact:	Firoze Shams	Utility Relocation Completed:	*
TxDOT PM:	Ray Wells	Anticipated Let Date:	*

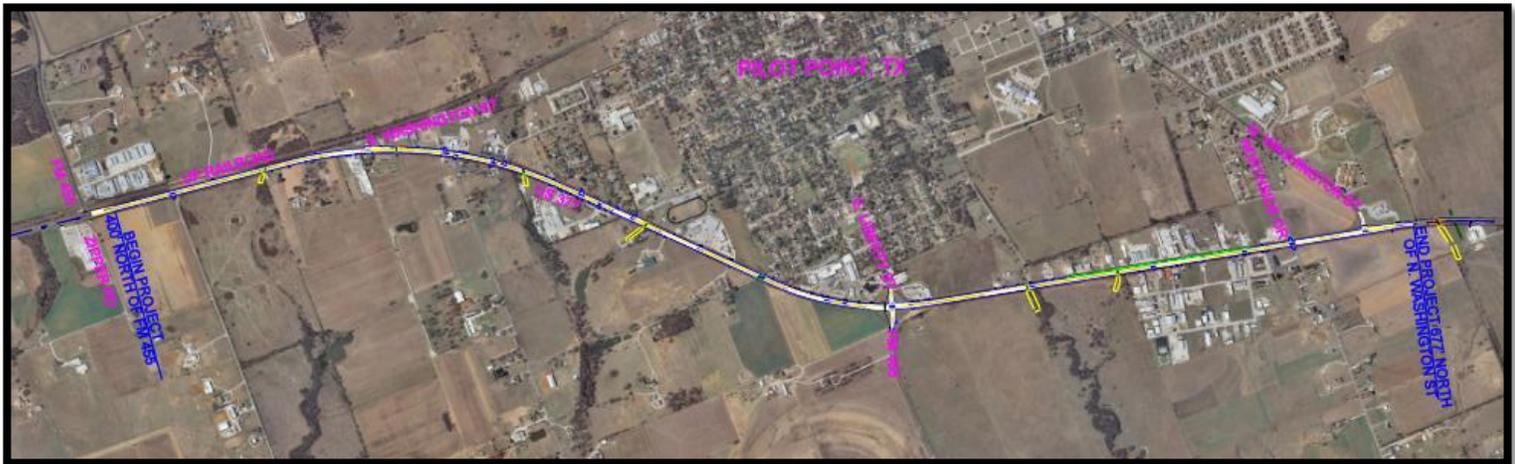

Current Activity:

- **ENV:** Environmental Clearance was provided on August 30, 2012.
- **Route Design Studies:** The four-lane divided section would cost approximately 60% more than the currently anticipated section (\$18 million versus \$12 million). The largest component of the increase is the cost of ROW, which is estimated at \$4.7 million.
- **PS&E:** Bridgefarmer made the 60% submittal on October 15, 2012.
- Bridgefarmer made the 90% submittal on December 10, 2012.
- A US 377 technical meeting has been scheduled for the third Monday of the month, quarterly.
- **See Status Report from Bridgefarmer.**

US 377 in Pilot Point, TX
CSJ: 0081-06-029

Engineer: Bridgefarmer & Associates, Inc.
Progress Report # 34
Period: February 2013 – March 2013

Activities during this Period

1. Continued project coordination with TxDOT, Denton County (ITS)
2. Continued project management activities
3. Met with TxDOT and TNMP at Denton County Area Office to go over the illumination design for the project and assign responsibilities for construction.
4. Met with Ray Wells and Chris Briggs at TxDOT Dallas District Office to go over the 95% SW3P comments.
5. Continued work towards finishing up the project



Firoze Shams, P.E., PTOE
Project Manager

US 377 Drainage Easements

- P.O. #131747 for \$13,500.00 was cut for TNP for drainage easement surveys for US 377 on December 14, 2012.
- Teague, Nall & Perkins is about 95% completed, and the final signed easements were submitted on January 15, 2013.
- ITS met with Commissioner Coleman on February 15, 2013, to discuss easements.
- Denton County drafted an ICA with Pilot Point for the cost to acquire the drainage easements to accommodate drainage improvements proposed by TxDOT.
- The ICA with Pilot Point was executed by Pilot Point and will be placed on Commissioners Court for consideration.

FM 455

CSJ:	0816-02-TBD	Begin Advanced Planning:	June 2010
Limits, Section A:	From FM 2450 to approx. ¾ mile west of IH-35	Complete Draft Env. Document:	*
Limits, Section B:	From approx. ¾ mile west of IH-35 to 1.5 miles east of IH-35/Marion Road	Schematic Approved:	*
Length:	5.3 miles	Clearance for Public Involvement:	*
Est. Const. Cost:	\$40 million	Public Hearing:	*
Project Description:	Widen two-lane rural roadway to four-lane urban roadway with turn lanes at IH-35	FONSI:	*
		ROW Acquisition Begins:	*
Firm:	Dannenbaum	Utility Relocation Completed:	*
Key Contact:	Danny Everett, Greg Vowels	Anticipated Let Date:	*



Current Activity:

- **ENV:** Environmental work is underway, including field investigations.
- **ROW:** Will begin once the project has been environmentally cleared.
- **PS&E:** Will begin once the schematic is sufficiently developed.
- FM 455 will be split into two sections for construction purposes. The construction estimate for the entire project is \$40 million. The estimate for the west project, Section A (from FM 2450 to approximately ¾ mile west of IH-35) is \$24 million. The construction estimate for the east project, Section B (from approximately ¾ mile west of IH-35 to 1.5 miles east of IH-35/Marion Road) is \$16 million. The project will not be split for the schematic and environmental phases.
- The LPAFA was fully executed on December 11, 2012.
- Dannenbaum submitted the schematic to the Dallas District on September 20, 2012.
- Comments received from TxDOT on November 29, 2012. Comment resolution meeting was held on December 18, 2012. Dannenbaum addressed comments and submitted a revised schematic for District review on February 26, 2013. **Dannenbaum received District review comments on March 25, 2013.**
- **See Dannenbaum status report.**

FM 455 Progress Report

3-22-13

C-S-J:	0816-02-TBD
Limits (From):	FM 2450
(To):	Marion Road
Length:	5.3 miles
Est. Const. Cost:	\$40 million
Description of Project:	Widen two lane rural roadway to a four lane urban roadway with turn lanes at IH 35

Past Month's Activities (March):


- Requested Detailed Traffic information (3/25/2013) from TxDOT- Expect to receive in 45 Days
- Received District review comments March 25, 2013

Next Month's Activities (April):

- Address District Comments

MAYHILL ROAD

Limits (From):	IH-35E	ROW Acquisition Began:	August 2011
(To):	US 380	ROW Acquisition Complete:	December 2013
Length:	3.9 miles	Design Complete:	December 2013
Est. Const. Cost:	\$56,670,566	Utility Relocations Complete:	December 2014
Project Description:	Widen existing two-lane roadway to four-lane, divided urban cross section	Award Construction Contract:	March 2014
Firm:	City of Denton	Construction Let Date:	January 2014
Key Contact:	Frank G. Payne, P.E.	Construction Complete:	Spring 2017

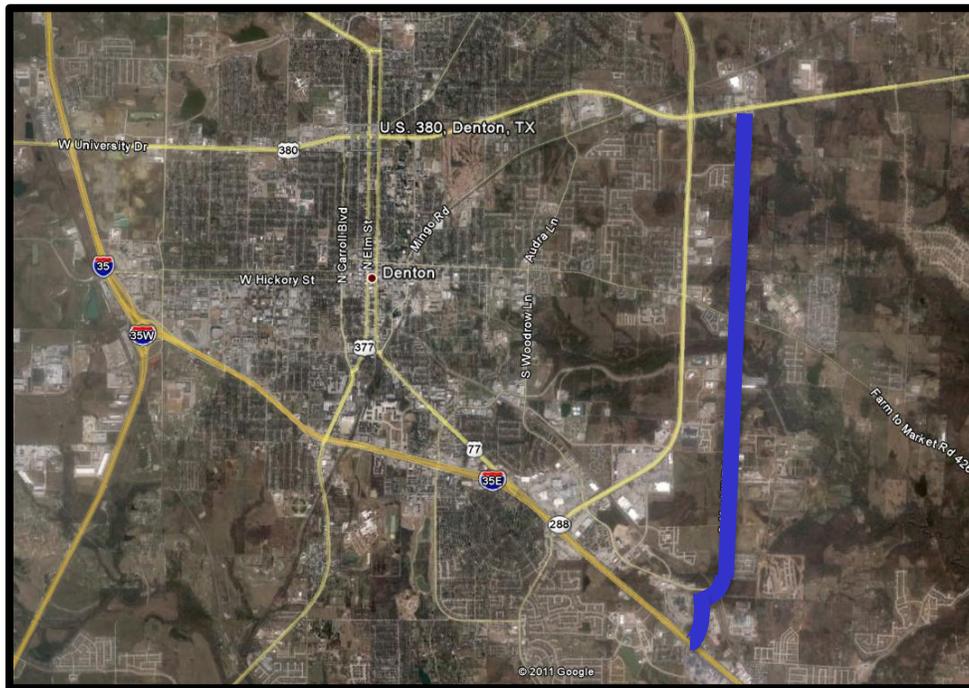

Current Activity

- The property acquisition process is proceeding with landowner meetings and offers. Acquisitions have been initiated on several properties.
- The City and design team are moving toward completion of the 60% design plans for the overall project.
- The City's primary goal at this point is to finalize the design set and to move forward with offers for Right-of-Way.
- The project website contains updates and project information: www.mayhillroad.com.

IH 35E ULTIMATE

- The Technical Work Group, the IH 35 Traffic Management Committee, met multiple times throughout the summer of 2012 to discuss some of the potential impacts to affected stakeholders. TxDOT took this information into account as they formulated the final Technical Provisions that were included in the Design Build contract.
- The Technical Work Group met for the final time on Friday, July 27, 2012.
- The final RFP was posted on the TxDOT website on July 13, 2012.
- TxDOT has submitted a TIFIA loan request for \$600 million.
- The TIFIA loan application was reworked to reflect a request for \$450 million. **The TIFIA loan request has been accepted; terms are being negotiated.**
- RFPs were submitted on November 12, 2012.
- AGL Constructors (Archer Western Contracts, LLC; Granite Construction Company; and The LANE Construction Company) was the firm selected. \$849 million nominal was the base bid.
- The first Notice-to-Proceed should be issued on May 15, 2013.
- **The second Notice-to-Proceed should be issued in August 2013.**
- **Alternative Technical Concepts are being considered for addition to the project. Traffic Revenue Studies will be completed to determine viability of options.**
- **ITS to provide additional information at meeting.**

DALLAS NORTH TOLLWAY, EXTENSION 4B

Limits:	From FM 428 extending north 7.7 miles to the county line
Length, Extension 4B:	7.7 miles
Ext. Const. Cost:	To be determined
Description:	To extend the Tollway north from US 380 to the Collin/Grayson County line by constructing a six-lane tollway with three northbound lanes and three southbound lanes; construction of six lanes of non-tolled frontage roads, including three lanes in each direction
Firm:	NTTA

Current Activity:

- On June 15, 2011, the NTTA Board approved the schematic design and environmental evaluation for the DNT Phase 4B/5A extension project.
- Planning has concluded for all phases of the DNT extension project.
- Denton County met with NTTA staff on May 2, 2012, regarding the initiation of design work on the DNT 4B project. The County and NTTA are working on a term sheet that will direct the process.
- Elizabeth Mow stated that a phased approach that fits within Denton County's budget should be submitted to the County by the end of the week of August 13, 2012.
- A meeting was held at NTTA on Friday, September 7, 2012, to discuss the proposed phased approach with Denton County.
- ITS received the draft ILA from NTTA and forwarded on Monday, September 24, 2012, to the civil attorney for review.
- The ILA was reviewed by NTTA, and it is expected to be presented to Commissioners Court for consideration on February 5, 2013. The ILA was executed by Denton County on February 5, 2013. **The ILA has been submitted to NTTA for execution.**

