



Precinct 1 Transportation Task Force


September 8, 2016

PROJECT STATUS UPDATES

- FM 2181 East-West page 2
- FM 2181 North-South..... page 4
- FM 720 North page 6
- FM 720 South page 8
- FM 2499, Section 5..... page 10
- FM 423 page 12
- FM 455..... page 14
- Mayhill Road page 15
- IH-35E Interim..... page 16
- Dallas North Tollway Extension page 17
- Denton County Thoroughfare Plan..... page 18
- US 377, Stewart/Arvin Hill page 19
- US 377 North..... page 20
- FM 2164/Union Hill at FM 455..... page 21
- US 380 page 22
- McReynolds Road, Sanger page 23
- Naylor Road..... page 24
- Doe Creek Road..... page 25
- RTC Agenda Items page 26

FM 2181 East-West

CSJ:	2054-02-016	FONSI:	January 28, 2008
Project Description:	Widen from two-lane to six-lane divided roadway	100% Plans:	December 2012
E/W Limits (From):	City of Denton/Corinth City Limits	ROW Acquisition Begins:	November 2009
E/W Limits (To):	IH-35E	Utility Relocations Complete:	March 2014
Firm:	Huitt-Zollars	Let Date:	May 8, 2013
Key Contact:	David Nufer	Construction Complete:	September 2016

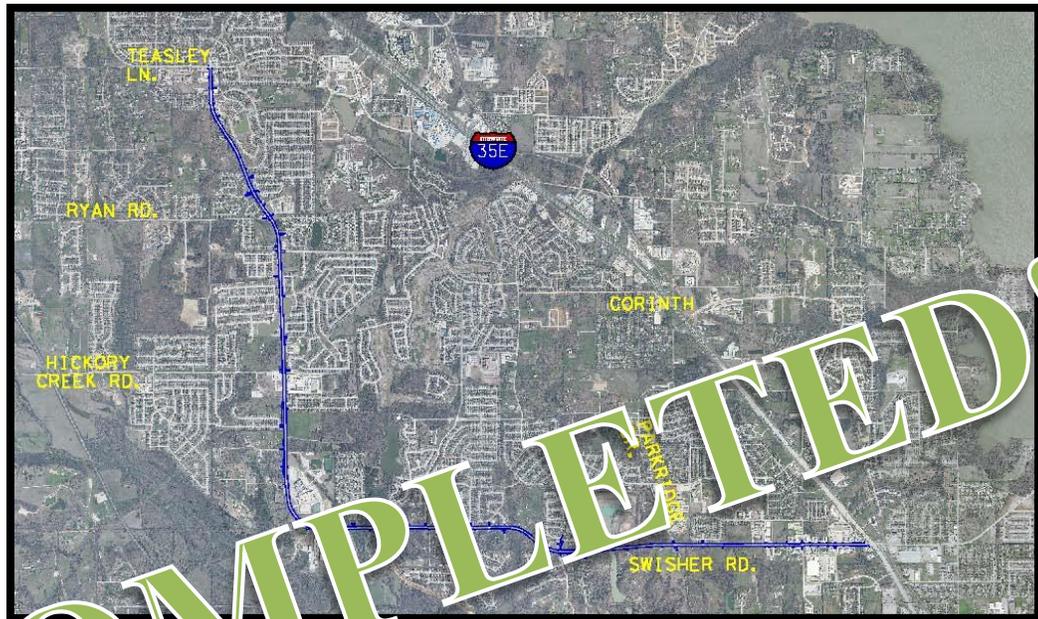

Current Activities

- **Construction:** The project let on May 8, 2013, and the contract was awarded to J.D. Abrams for \$24,679,639.00. There are approximately 416 working days and 24 months of barricades.
- **See attached TxDOT construction report.**
- Final traffic switch made on May 5, 2016.
- A ribbon-cutting ceremony was held at the northwest corner of IH-35E and FM 2181 on July 6, 2016.

TxDOT Monthly Project Report for Precinct 1 Task Force

Date of report: September 1, 2016

Report prepared by: Mark Wiley

Project: **STP 2013(667) MM, Etc.**

Control: **2054-02-016, Etc.**

Highway: **FM 2181**

Limits: From: West of FM 2499 (Barrel Strap Road)

To: West of IH 35E frontage road in Corinth

Contractor: **J.D. Abrams, L.P.**

TxDOT Project manager: Mark Wiley

Phone: (940) 284-0545

Contractor's Superintendent: Hayden Mitchell

Phone: (214) 354-9077

Date Work Began: February 17, 2014

Anticipated Completion Date: September, 2016

Current Activities:

Current activities include: Awaiting acceptance.

Narrative description of last month's activities: All lanes of traffic have been opened. Working on traffic signals.

Narrative description of activities planned for next month: Awaiting acceptance

Traffic issues: None


Plans for changes in traffic patterns: None

Item(s) of work currently controlling project completion: NA

Other items of significance: N/A

FM 2181 North-South

CSJ:	2054-02-015	FONSI:	January 28, 2008
Project Description:	Widen from two-lane to six-lane divided roadway	100% Plans:	*
Limits	From City of Denton/Corinth City Limits to Lillian Miller	ROW Acquisition Began:	November 2009
Construction Cost Estimate:	\$30 million	Utility Relocations Complete:	*
Firm:	Huitt-Zollars	Let Date:	August 2017
Key Contact:	David Nufer	Construction Complete:	*

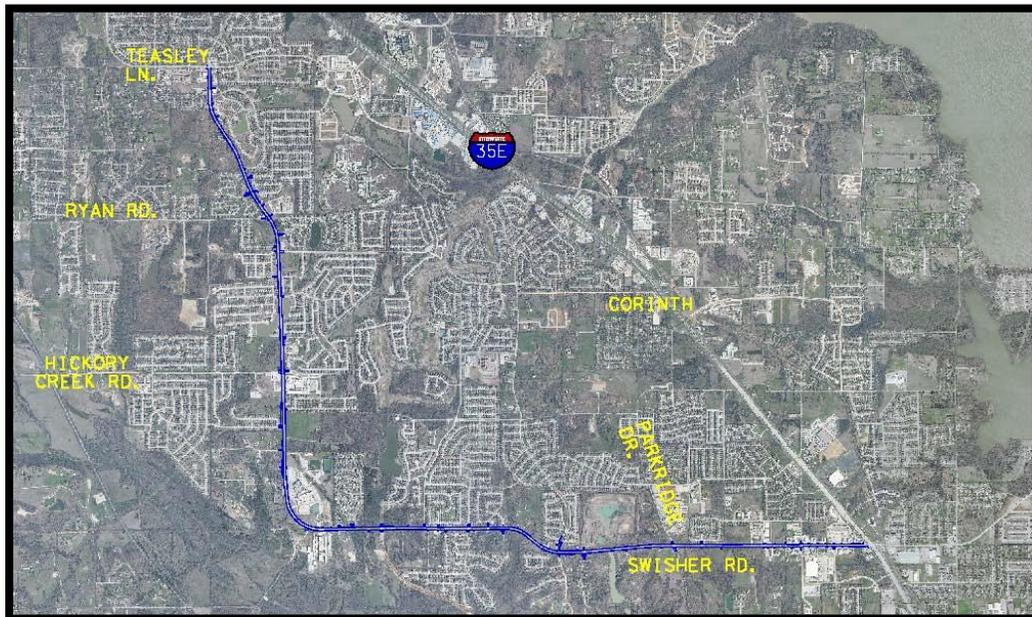

Current Activity:

- **ROW:** Acquisition is complete.
- **PS&E:** Huitt-Zollars met with TxDOT to review outstanding issues and requested meeting with Freese & Nichols and Teague Nall & Perkins (Denton ISD consultant) to discuss easements and other design issues in the vicinity of the high school. Huitt-Zollars is coordinating with Freese & Nichols on utility relocations. Huitt-Zollars met with TxDOT, ITS, City of Denton, and Freese & Nichols to discuss possible design changes to plans to reduce costs associated with relocations of city service lines. Huitt-Zollars requires receipt of 60% level utility relocation plans from City of Denton (Freese & Nichols) in order to proceed with 95% PS&E submittal. Huitt-Zollars is working toward completion of 95% PS&E and plans to submit to TxDOT before the end of September 2016, depending upon receipt of design plans from both City of Denton (Freese & Nichols) and DISD (Teague, Nall & Perkins).
- **Utilities:** TxDOT is working with the City of Denton to include city utilities as part of the construction project at a fixed cost. See attached utility update.
- **Funding:** The project is funded with \$18 million in Proposition 1 (CAT 2), \$2.1 million in Proposition 1 (CAT 11), and \$3.8 million in Proposition 1 (CAT 1).

Utility Coordination Report: FM 2181

August 22, 2016

City of Denton – Will have 60% plans completed in the beginning of September. Utility will be incorporated into the construction contract.

Frontier Communications – Anticipated completion in December 2016.

Charter Communication – Anticipated completion in October 2016.

CoServ Gas – Working on design. No completion date available at this time.


DME – Complete from Lillian Miller to Hickory Creek. Working on Overhead from Hickory Creek to Guyer High School. Still under design from Guyer south to Bluebonnet Drive.

UTRWD – Potholing 2 existing crossings and working on design for an additional crossing. No completion date available at this time.

Grande – Working on design. Talking to DME and Oncor to get on poles. No completion date available at this time.

FM 720 NORTH

CSJ:	1567-01-037	Schematic Approved:	March 2014
Limits :	From US 380 to Martop Lane	Environmental Clearance:	March 11, 2015
Est. Const. Cost:	\$18,600,000	100% PS&E:	February 2017
Funding:	\$17 million in Proposition 1 Funds	ROW Complete:	November 2017
Project Description:	Widen two-lane rural roadway to six-lane divided urban	Utilities Completed:	February 2018
Firm:	TxDOT	Let Date:	June 2018
Key Contact:	Mike Hainline	Construction Completion:	*

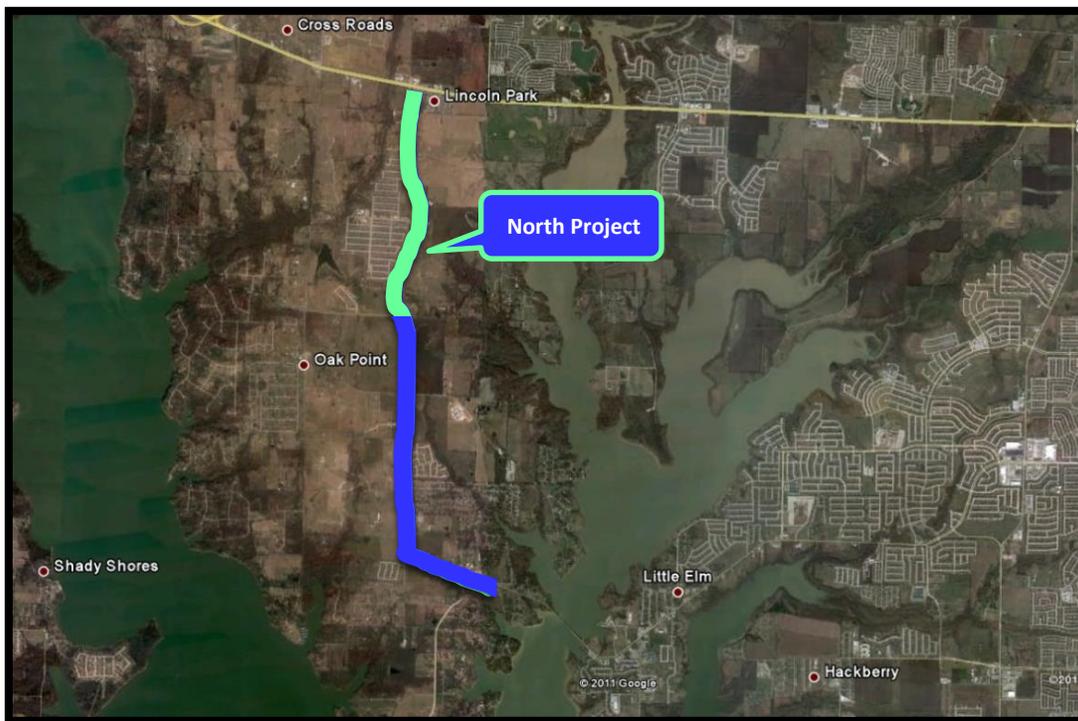

Current Activities:

- See attached TxDOT status report.
- The north project was split from the south project after investigating the impacts of two large water lines on the west side of FM 720 north of Martop to 0.5 miles south of US 380. Due to the cost and time to relocate the water lines, it was determined that the north FM 720 project would be delayed to allow alternative FM 720 alignments that avoid the water lines to be considered.
- **ROW:** The completion date for right-of-way is November 2017 due to the issues surrounding the Oak Grove Cemetery parcel.



**FM 720 North: From Martop Road to US 380
CSJ 1567-01-037
Denton County**

PROJECT STATUS AS OF Monday, September 12, 2016:

COMPLETED MILESTONES:

Schematic Revisions Begin: April 1, 2013

Revised schematic approved: Nov 2013

MAPO/Public Meeting: April 2014

Environmental Re-Eval Checklist State Approval: July 2014

30% PS&E (Design) Plans: October 2014

ROW map complete: October 2014

Environmental Clearance (Re-eval): March 11, 2015

60% PS&E (Design) suitable for Utility relocation plans: June 16, 2016

FUTURE MILESTONES:

ROW acquisition: Feb 2015 thru Spring/Summer 2017; 27 total parcels, status: 17 parcels acquired, 10 parcels in Eminent Domain;

Cemetery issues (Parcel 15): received right of entry to begin archaeological and historical investigation. However, issues remain with access and conditions imposed by adjacent property owner (Parcel 13) to allow State forces to do investigations. ED Hearing for Parcel 13 scheduled for September 12. Parcel 13 acquired by October. Above investigation for cemetery to commence shortly thereafter. If no graves found in Parcel 15 area, then legal proceedings can begin to remove cemetery designation, and acquisition can begin. Estimate Parcel 15 clear by Spring/Summer 2017 if no graves found.

Utility relocations: estimate December 2016 thru January/February 2018


95% PS&E (Design): October 2016

100% PS&E (Design): February 2017

Start construction: 2 months after Project Letting; accelerated construction specifications will be included in the construction plans.

FM 720 SOUTH

CSJ:	1567-01-025	Complete Draft CE:	March 2006
Limits (From):	Eldorado Parkway	Schematic Approved:	October 2007
(To):	South of Martop Road	FONSI:	December 14, 2011
Est. Const. Cost:	\$15,597,320	100% PS&E:	November 2013
Project Description:	Widen two-lane rural roadway to six-lane divided urban	ROW Acquisition Complete:	June 2014
		Utility Relocations Complete:	November 2015
Firm:	TxDOT	Let Date:	February 4, 2014
Key Contact:	Mike Hainline	Construction Completion:	February 2017

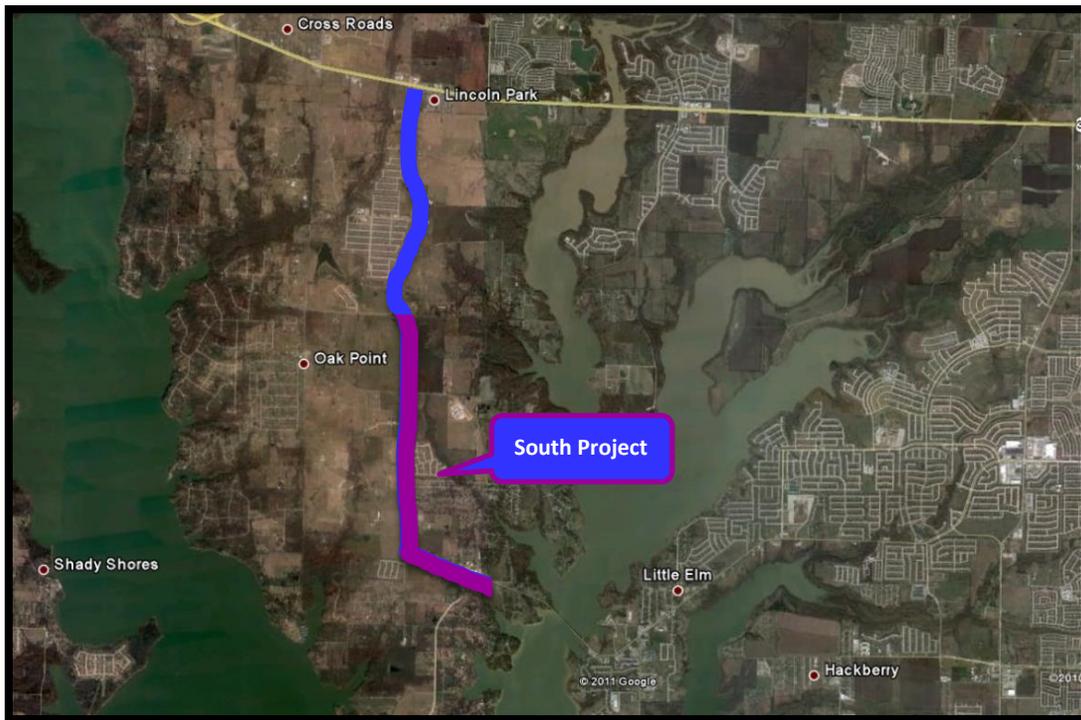

Current Activities:

- **Utilities:** Relocations are now complete, with the exception of Little Elm, which is a new utility and is being coordinated with the contractor. Suddenlink has an additional location in conflict. They are working on approvals for relocation and are not able to provide start and completion date for relocation. **Suddenlink relocated line in conflict.**
- **Construction:** The project let on February 4, 2014. The project was awarded to Haydon Building Corporation, with a low bid of \$15,597,320.25, approximately 0.6% over the estimate. There are 420 working days and 20 months of barricades. Construction began on November 9, 2015. **See TxDOT construction report.**

TxDOT Monthly Project Report for Precinct 1 Task Force

Date of report: September 6, 2016

Report prepared by: Richard Williford

Project: **C 1567-1-25**

Control: **1567-01-025**

Highway: **FM 720**

Limits: From: Eldorado Parkway (FM 720)

To: South of Martop St.

Contractor: **Haydon Building Corp.**

TxDOT Project manager: Richard Williford

Phone: (940) 453-1716

Contractor's Superintendent: Matt Gilliland

Phone: (214) 984-1598

Date Work Began: November 9, 2015

Anticipated Completion Date: February 3, 2017

Current Activities:

Current activities include: SW3P, roadway drainage, cross drainage, excavation of roadway, roadway embankment, reinforced concrete pipe, inlet bottoms, placing cement subgrade and flex base to Hill Lane.

Narrative description of last month's activities: SW3P, roadway drainage, cross drainage, excavation of roadway, roadway embankment, reinforced concrete pipe, inlet bottoms, placing cement to subgrade flex base, and concrete paving from Martop to McCormack.

Narrative description of activities planned for next month: Preparing ROW, SW3P, roadway drainage and cross drainage – culvert roadway embankment, flex base subgrade and asphalt and concrete paving.

Traffic issues: None

Plans for changes in traffic patterns: None at this time

Item(s) of work currently controlling project completion: None

Other items of significance: None at this time

FM 2499, Section 5

CSJ:	2681-01-012
Limits (From):	FM 2181
(To):	IH-35E
Length:	2.97 miles
Construction Cost:	\$34,857,000
Description:	Construct six-lane divided urban roadway
Firm:	Halff Associates
Key Contact:	Mike Romanowski
FONSI:	November 3, 2010
Environmental Re-Eval:	April 25, 2014
100% PS&E:	January 2012
ROW Complete:	February 2014
Utilities Relocated:	Phase I completed March 2015; Phase II complete in October 2016
Project Tracker Let Date:	July 8, 2014
Construction Complete:	November 2017



Current Activity:

- **PS&E:** Final 100% bid set was submitted in May 2014.
- **Utilities:** NGG and Charter are the remaining utilities on Phase 2. NGG is relocating high pressure gas line and anticipates being clear in mid-September. Charter has approved plans but has not begun relocation. All utilities are clear in Phase 1.
- **Funding:** This project is fully funded with Regional Toll Revenue.
- **Construction:** The project let on July 8, 2014. The low bidder was Webber, LLC, in the amount of \$34,857,000.00, which was 3% over the estimate. The contract calls for 505 working days and 24 months of barricades. Construction began on April 20, 2015. See attached TxDOT construction report.

TxDOT Monthly Project Report for Precinct 1 Task Force

Date of report: September 1, 2016

Report prepared by: Mark Wiley

Project: **C 2681-1-12**

Control: **2681-01-012**

Highway: **FM 2499**

Limits: From: FM 2181 north

To: IH 35E

Contractor: **Webber, LLC**

TxDOT Project Manager: Mark Wiley

Phone: (940) 387-1414

Contractor's Superintendent: Daniel Hoyet

Phone: (469) 203-1494

Date Work Began: April 20, 2015

Anticipated Completion Date: November 2017

Current Activities:

Current activities include: Continuing cutting grade located at 111+00 and 126+00 and installing culvert 6.

Narrative description of last month's activities: Placement of shafts for noise walls, retaining walls, bridge drill shafts, form caps, and abutments for bridge. Continuing cutting grade located at 111+00 and 126+00 and installing culvert 6.

Narrative description of activities planned for next month: Bridge access and drill shafts for abutment #1. Continue sound wall and retaining wall installations.

Traffic issues: None at this time

Plans for changes in traffic patterns: None at this time

Item(s) of work currently controlling project completion: Placement of noise and retaining walls. Placement of drainage systems, phase I.

Other items of significance: N/A

FM 423: NORTH

CSJ:	1315-02-009
Limits (From):	Stewart Creek Road
(To):	US 380
Length:	6.91 miles
Construction Cost:	\$29,826,069.71
Description:	Construct four- to six-lane divided urban roadway
Engineering Firm:	Jacobs Engineering
ROW Acquisition Began:	December 2010
ROW Acquisition Complete:	July 2012
Utility Relocations Began:	July 2011
Utility Relocations Complete:	October 2015
Let Date:	September 11, 2013
Construction Began:	October 8, 2014
Construction Complete:	August 2017



Current Activity:

- **ROW:** ROW acquisition is complete.
- **Utilities:** Utility relocations are complete. Additional conflicts with CoServ Electric, Suddenlink, Grande, and AT&T due to added left-turn lane. TxDOT coordinating with utilities to remove conflicts.
- **PS&E:** 100% Plans have been completed.
- **Construction:** Project let on September 11, 2013, and was awarded to MCM, with a bid of \$29,826,069.71. There are 29 months of barricades. See attached construction report.

TxDOT Monthly Project Report for Precinct 1 Task Force

Date of report: September 6, 2016

Report prepared by: Richard Williford

Project: **C 1315-2-9**

Control: **1315-02-009**

Highway: **FM 423**

Limits: From: US 380

To: 0.8 miles south of FM 2934 (Eldorado Parkway)

Contractor: **MCM**

TxDOT Project manager: Richard Williford

Phone: (940) 453-1716

Contractor's Superintendent: Alex Bernard

Phone: (575) 635-1357

Date Work Began: October 8, 2014

Anticipated Completion Date: August 2017

Current Activities:

Current activities include: Placing concrete for sidewalks and ADA ramps, bridge crew working on southbound bridge columns and caps working on roadway excavation and subgrade for lime extending cross drainage, placing block sod, SW3P, and reinforced concrete pipe, working on subgrade for northbound concrete paving.

Narrative description of last month's activities: Placing concrete for sidewalks and ADA ramps, placing drilled shafts for permeant signals, working on subgrade for northbound concrete paving, RCP, headwalls, inlet bottoms, constructing Panther Creek Parkway, SW3P, and clean-up on project.

Narrative description of activities planned for next month: MCM working on constructing southbound bridge, lime subgrade, cross drainage, Panther Creek Parkway sidewalks, ADA ramps, and block sod.

Traffic issues: None

Plans for changes in traffic patterns: Traffic is due to be placed on newly constructed southbound lanes when lanes are completed.

Item(s) of work currently controlling project completion: None

Other items of significance: AT&T, CoServ Electric and Gas utilities conflicting with roadway near Eldorado.

FM 455

CSJ:	0816-02-072	Schematic Approval:	Re-approval received March 1, 2016
Limits, Section A:	From FM 2450 to approx. ¾ mile west of IH-35	Public Hearing:	October 2016
Limits, Section B:	From approx. ¾ mile west of IH-35 to 1.5 miles east of IH-35/Marion Road	Environmental Clearance:	March 2017
Est. Const. Cost:	\$40 million	100% Plans:	*
Project Description:	Widen two-lane rural roadway to four-lane urban roadway with turn lanes at IH-35	ROW Complete:	July 2019
		Utilities Complete:	July 2020
Firm:	Dannenbaum	Let Date:	October 2020
Key Contact:	Danny Everett	Construction Completion:	*



Current Activity:

- **ENV:** Public meeting was held on June 23, 2015, in Sanger, Texas. Dannenbaum re-submitted for District review the biological evaluation form and Waters of the U.S. Technical Report. Report has undergone third district review. Community Impacts Assessment Technical Report has been reviewed by District. Dannenbaum is addressing ENV comments. Archaeological site survey report was submitted on August 18, 2016, and is undergoing District review. Air Quality and Traffic Noise Analysis Reports have been reviewed. Dannenbaum is addressing District comments. Indirect/Cumulative Impacts Technical Report and Environmental Assessment are currently being drafted. Hazardous Materials ISA and Water Resources are approved.
- **Schematic:** Schematic was re-approved by TxDOT on March 1, 2016.
- **ROW:** Base map for survey is complete, and partial ROW parcel submittal was made on August 25, 2016. Continuing ROW mapping and will begin submitting final parcels for TxDOT review.
- **PS&E:** Dannenbaum is preparing to begin PS&E. Dannenbaum received preliminary SUE. Level B SUE submitted to TxDOT. Beginning work on Level A SUE test holes. Dannenbaum coordinated with TxDOT, Denton County, City of Sanger, and Sanger ISD on access to Chisholm Trail Elementary from FM 455. Received approval from Sanger ISD for access to Chisholm Trail Elementary School from FM 455. Preparing to begin PS&E.
- **Funding:** FM 455 is listed as a Proposition 1 project with funding totaling \$30.9 million.

IH 35E INTERIM


- Construction began on October 28, 2013.
- **FM 407:** Deck placement for the bridge over FM 407 is complete. Concrete paving of the northbound main lanes over FM 407 is ongoing. Grading and pavement work to finish the intersection is underway. Additional lanes are expected to open by mid- to late September. Hardscape work will continue into the fall.
- **Garden Ridge Boulevard:** The bridge is expected to fully open to traffic this fall. The southbound I-35E exit ramp to Garden Ridge Boulevard shifted north about 500 feet to its original location in August.
- **Copperas Branch Park:** Work on the Copperas Branch Park East has been completed, and the park was turned over to the City of Lewisville in August.
- **Highland Village Road:** Highland Village Road has been temporarily closed through September 9 as crews work to elevate the roadway approximately 8 feet to meet the southbound frontage road.
- **New southbound Lewisville Lake Bridge:** Final touches are being placed on the Lewisville Lake Bridge. A milestone celebration was held on September 7, 2016. Southbound traffic will be placed on the bridge by 8:00 a.m. Saturday, September 10, and northbound traffic will be placed on the bridge by 8:00 a.m. Saturday, September 17. Once northbound traffic is placed on the new bridge, all but one lane of the original bridges will close to traffic until 2017. The single lane will be used as the exit ramp to Lake Dallas Drive. The exit will be located near Garden Ridge Boulevard.
- **Swisher Road:** Northbound I-35E exit ramp 459, north of Swisher Road, will shift approximately 1,500 feet north in September. A new northbound exit ramp will be constructed north of Swisher Road and open later this year.
- **Corinth Parkway Bridge:** Drainage and frontage road work continue at Corinth Parkway.
- **Post Oak Bridge:** Connectivity for the Post Oak bridge is scheduled to be restored in September. This will include one lane in each direction. The bridge is scheduled for completion next year.
- **Oak Drive:** With the closure of South Denton/Lake Dallas Drive bridge, work has begun on the new I-35E bridge over Oak Drive. North- and southbound I-35E traffic will shift onto the west side of the new bridge over Oak Drive in September.
- **North Denton/Lake Dallas Drive:** The northbound frontage road from Janet Court to the intersection of Lake Dallas Drive and the frontage road has been closed and is scheduled to reopen in late 2016.
- **Turbeville:** One lane in each direction of the new extension of Turbeville/Hundley Drive is now open. The remaining lanes will open in 2017.
- **Mayhill Road:** The north- and southbound I-35E mainlanes south of Mayhill Road shifted onto new pavement in the median of the interstate in August.
- **Loop 288:** The southbound exit ramp to Loop 288 will be relocated north about 1,000 feet in September.
- **US 77/Dallas Drive:** The US 77 bridge is slated for completion by October. Northbound I-35E traffic will be placed onto the new bridge after completion.
- **North Texas Boulevard:** Connectivity across the North Texas Blvd. bridge has been restored with one lane in each direction and a dedicated turn lane. Work constructing the remaining portions of the bridge will continue into the fall.
- **McCormick Street:** The northbound frontage road north of McCormick Street is scheduled to shift into its final configuration in October. Collier Street will reopen to the northbound frontage road soon after.

DALLAS NORTH TOLLWAY, EXTENSION 4B

Limits:	From FM 428 extending north 7.7 miles to the county line
Length, Extension 4B:	7.7 miles
Ext. Const. Cost:	To be determined
Description:	To extend the Tollway north from US 380 to the Collin/Grayson County line by constructing a six-lane tollway with three northbound lanes and three southbound lanes; construction of six lanes of non-tolled frontage roads, including three lanes in each direction

Current Activity:

- **ROW:** NTTA has all but two donation agreement signed by the property owners. The outstanding agreements are with Bunch and Clark. NTTA continues to work with property owners to secure the donation agreement. All Denton County property owners have signed agreements. NTTA continues to survey the right of way and adjacent property along the DNT 4B in preparation for the design.
- The notice to proceed with the design was issued on December 10, 2014.
- Burns & McDonnell submitted the 60% plans to NTTA in early April 2016. NTTA is reviewing plans. Value engineering study underway. The 60% plan approval to be completed after value engineering study is completed.
- NTTA approved Burns & McDonnell to proceed with design of southbound frontage road in current contract. Denton County will modify existing ICA with NTTA upon receipt of additional funding for the project.
- COG staff concurred with use of RTR funds for extension of southbound frontage road through Celina to FM 428. ITS staff will process TIP modification to obligate funds. Denton County submitted a TIP modification for \$5,000,000 for DNT 4B Extension on July 23, 2015. RTC approved additional funding for the DNT frontage road in the October meeting. TIP modification was approved by FHWA. ITS is coordinating with TxDOT on an LPAFA for the project funding adjustment. ITS is working with the Denton County civil attorney's office on an ICA amendment to reflect the increase in funding. **LPAFA was approved by commissioners court on August 30, 2016.**
- ITS met with NTTA to discuss the project on March 1, 2016.

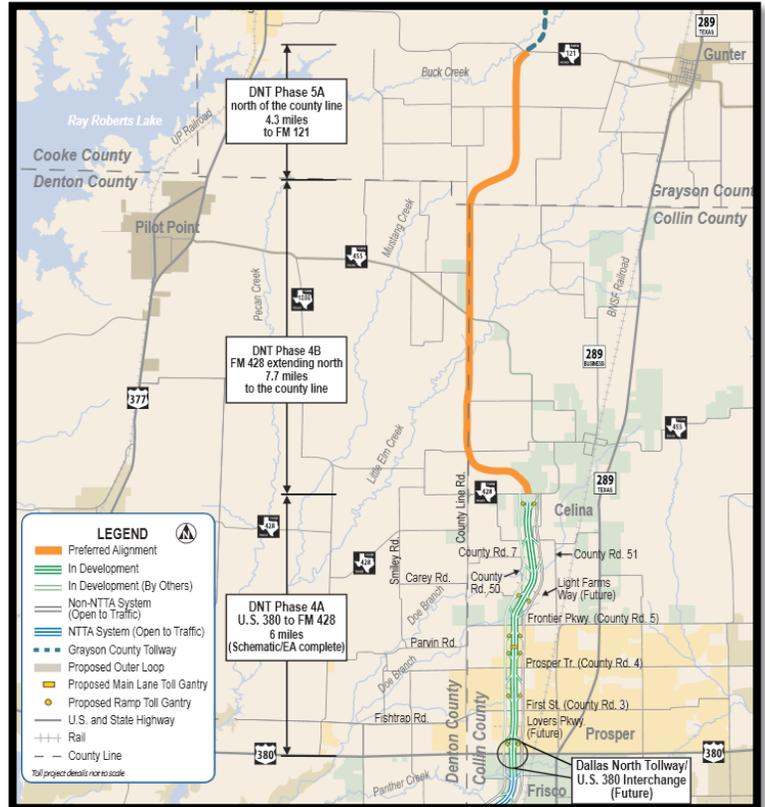


DENTON COUNTY THOROUGHFARE PLAN

- Freese & Nichols continued collaborating with NCTCOG regarding particular network attributes and connections for modeling the enhanced network to represent the Draft Thoroughfare Plan.
- Freese & Nichols continued writing draft report sections on existing conditions modeling and initial description of Thoroughfare Plan.
- Freese & Nichols reviewed draft thoroughfare plan with select cities regarding updates to their thoroughfare plans.
- Freese & Nichols completed review of NCTCOG adaptation of 2035 MTP model for updated Denton County thoroughfares.
- Freese & Nichols delivered draft report document to ITS for review on June 19, 2015. ITS reviewed draft report and provided input to Freese & Nichols on July 10, 2015. Freese & Nichols has reviewed comments and is incorporating, as well as working on overall content and action items.
- Freese & Nichols received new information from the City of Fort Worth and completed minor updates to the thoroughfare plan map.
- FNI met with Commissioner Coleman on November 16, 2015, to review the thoroughfare plan map and discuss the major changes to the existing network.
- ITS is coordinating meetings with the other county commissioners to review the thoroughfare plan map.
- FNI to incorporate the commissioners' comments into the final thoroughfare plan documents.
- FNI resubmitted draft thoroughfare plan report to ITS on January 12, 2016. ITS responded with additional comments and corrections.
- Awaiting review comments from commissioners and any further changes from cities.
- Meeting with Judge Horn and Commissioner Eads held on April 7, 2016.
- Meeting with Commissioner Marchant and Commissioner Mitchell held on April 20, 2016.
- ITS and Freese & Nichols met with the City of Sanger on March 26, 2016, and Pilot Point on April 20, 2016, to discuss the thoroughfare plan.
- ITS met with Krugerville on May 17, 2016, to discuss the thoroughfare plan.
- ITS met with Oak Point on May 19, 2016, to discuss the thoroughfare plan.
- ITS met with Lakewood Village on May 25, 2016, to discuss the thoroughfare plan.
- ITS is coordinating a meeting with Frisco to discuss the thoroughfare plan.
- Recently incorporated review comments from Pilot Point and Sanger.
- FNI awaiting additional feedback from cities.
- ITS met with the City of Frisco on July 14, 2016, to review the thoroughfare plan.
- **ITS is coordinating a meeting with the City of Denton to review the thoroughfare plan.**

US 377: Intersection at Stewart/Arvin Hill

Limits:	US 377 at Stewart and Arvin Hill Road
Ext. Const. Cost:	\$4,000,000 (total project)
Description:	Realign the roadway to create one intersection, instead of two on US 377 at the Stewart and Arvin Hill intersections (this is part of larger Arvin Hill project to widen roadway and improve drainage)
Firm:	TranSystems

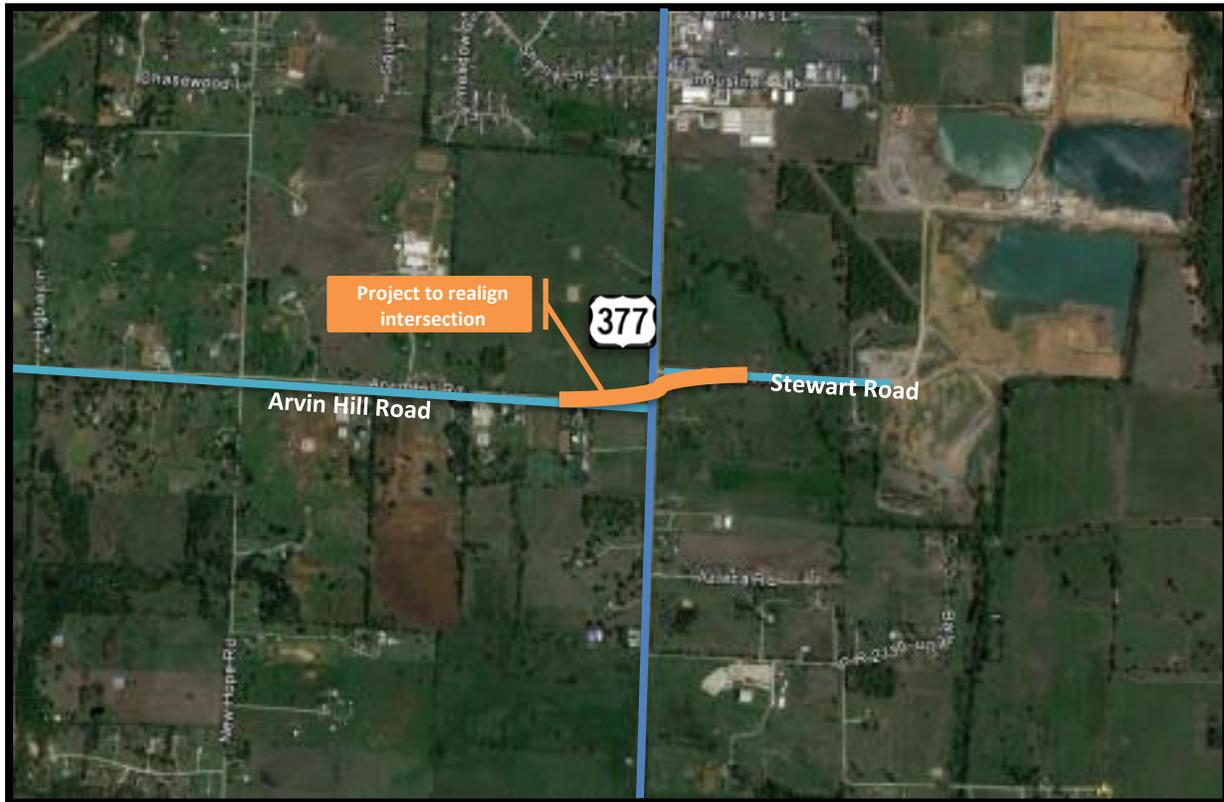


Current Activity:

- The county issued a supplemental agreement with the engineer to include the design of Arvin Hill from Red Mesa to Highway 377, including the intersection of Arvin Hill and Highway 377. Consultant submitted 30% plans to the county for the Arvin Hill portion. County returned comments on 30% plans to engineer. Engineer has completed 60% plans, which include the realignment of Arvin Hill to US 377. The intersection improvements of US 377/Arvin Hill/Stewart are in the schematic phase.
- The design of Rock Hill Road to Red Mesa Trail has been completed.
- Design on the intersection has begun.
- **ROW:** One parcel is required for acquisition on this project. Denton County revised the ROW across the property at the request of the owner; however, the owner is no longer cooperating. Denton County has advised the property owner's attorney that the next step is condemnation and using the original ROW alignment. Condemnation is proceeding to trial. Trial has been set for September 12, 2016.

US 377 North

CSJ:	*	Schematic Approval:	*
Limits:	From US 380 to Grayson County Line	Environmental Clearance:	*
Est. Const. Cost:	*	100% Plans:	*
Funding:	*	ROW Acquisition Complete:	*
Project Description:	Widen two-lane rural roadway to four-lane facility	Utility Relocations Complete:	*
Firm:	*	Let Date:	*
Key Contact:	*	Construction Completion:	*

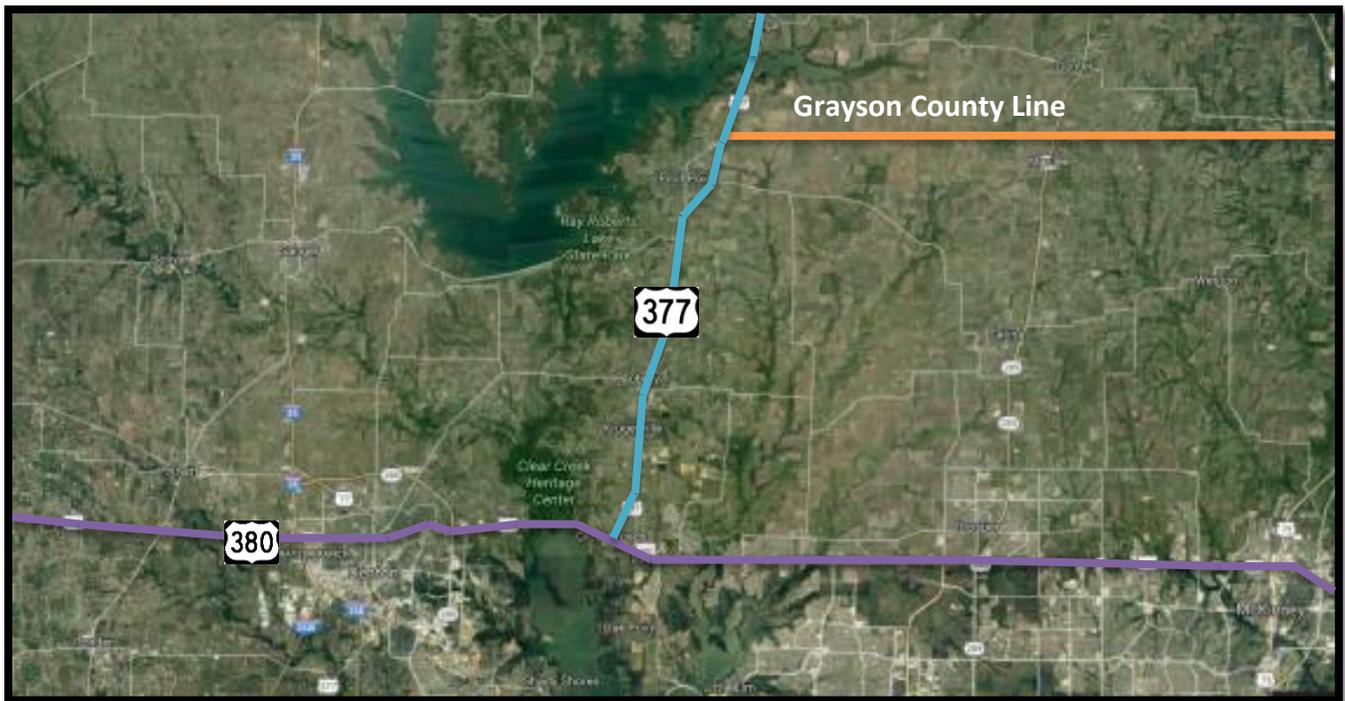

Current Activity:

- ITS met with TxDOT the first week of July 2013 to discuss the project.
- ITS met with TxDOT on Monday, July 29, 2013, to review the project plans.
- ITS met with TxDOT on Tuesday, January 21, 2014, to discuss the project and possible TxDOT participation. Anticipate project needing a Categorical Exclusion. Currently, TxDOT Dallas does not have any safety (CAT 5) or maintenance (CAT 1) funding for this type of job.
- ITS met with TxDOT Dallas District regarding future funding opportunities. It was decided that Denton County should begin advanced planning to get project ready for Proposition 7 funding in FY 2018-2019.
- ITS met with TxDOT on June 30, 2016, to discuss the scope of the advanced planning effort on US 377 from US 380 to the Grayson County line.
- **ITS met with TxDOT on August 16, 2016, to discuss the project.**

FM 2164/Union Hill at FM 455

CSJ:	0816-02-079	Schematic Complete:	April 7, 2016
Limits:	Intersections of FM 2164 and Union Hill at FM 455	EA Complete:	August 2, 2016
Est. Const. Cost:	\$1,006,008	ROW Complete:	September 2017
Project Description:	Realign Intersection of FM 2164, FM 455, Union Hill	Utilities Complete:	January 2018
Firm:	LTRA	Let Date:	March 2018
Key Contact:	Massoud Manesh	Construction Complete:	*

Current Activity:

- **Schematic:** Schematic was approved by TxDOT on April 7, 2016.
- **Environmental:** Environmental clearance received on August 2, 2016.
- **PS&E:** TxDOT requested that LTRA go through plan submittal process and submit 60% plans to TxDOT for review prior to 95% plan submittal. The 60% plans were submitted to TxDOT for review on July 19, 2016.
- **ROW:** LTRA submitted proposed ROW map and parcel descriptions to Denton County. There are 5 parcels to be acquired. ROW agreement between TxDOT and Denton County has been executed. ROW CSJ is 0816-02-080. LTRA addressed ROW map comments and submitted final ROW documents to TxDOT on August 12, 2016.
- **Utilities:** LTRA continues coordination with utility companies. Performing SUE in the field to better locate utilities in conflict. LTRA has sent out right of entry letters to property owners to obtain Level A SUE test holes.



US 380

Limits:	0135-10-050 (from US 377 to Collin County Line; 0135-10-057 (from Loop 288 to US 377))	Schematic Approval:	October 2016
Description:	Widen existing roadway from 4-lane to 6-lane divided with intersection improvements	Environmental Completion:	April 2017
Ext. Const. Cost:	\$90 million	ROW Complete:	June 2019
Firm:	AECOM	Utilities Complete:	December 2020
Key Contact:	Bruce Nolley, TxDOT; Rajesh Janarthanan AECOM	Let Date:	February 2021




Current Activity:

- **Schematic:** AECOM submitted schematic plans to TxDOT for review in December.
- **AECOM** worked on 10-foot sidewalk option. Prepared plan view and created cross sections. Prepared additional typical sections and cost estimates. Made minor refinements to cross street profiles. Completed and submitted traffic and drainage reports.
- There will be five grade separations at FM 720, FM 423, Navo, Teal, and Legacy.
- **ENV:** The public meeting was held on May 12, 2016. AECOM prepared and submitted public meeting summary report to TxDOT. AECOM is continuing work on the EA document.
- **ROW:** AECOM finalized the proposed ROW based on the revised design and is preparing additional ROE letters based on revised ROW for ENV survey. AECOM performed additional survey work.
- **Utilities:** AECOM prepared and completed SUE drawings.
- **Funding:** For CSJ -050, TxDOT has identified \$47.1 million in Proposition 1 funds and \$14 million in STP-MM for a total of \$61.1 million; for CSJ -057, TxDOT has identified \$13 million in Proposition 1 funds.

McReynolds Road, Sanger

Limits:	From Jones Street to FM 2164
Description:	Reconstruct and widen roadway to twelve-foot lanes with four-to-one safety slopes and construction of storm water facilities to convey a 100-year flood
Construction Cost:	\$6,900,000
Firm:	Pacheco Koch
Key Contact:	Neal Welch, City of Sanger

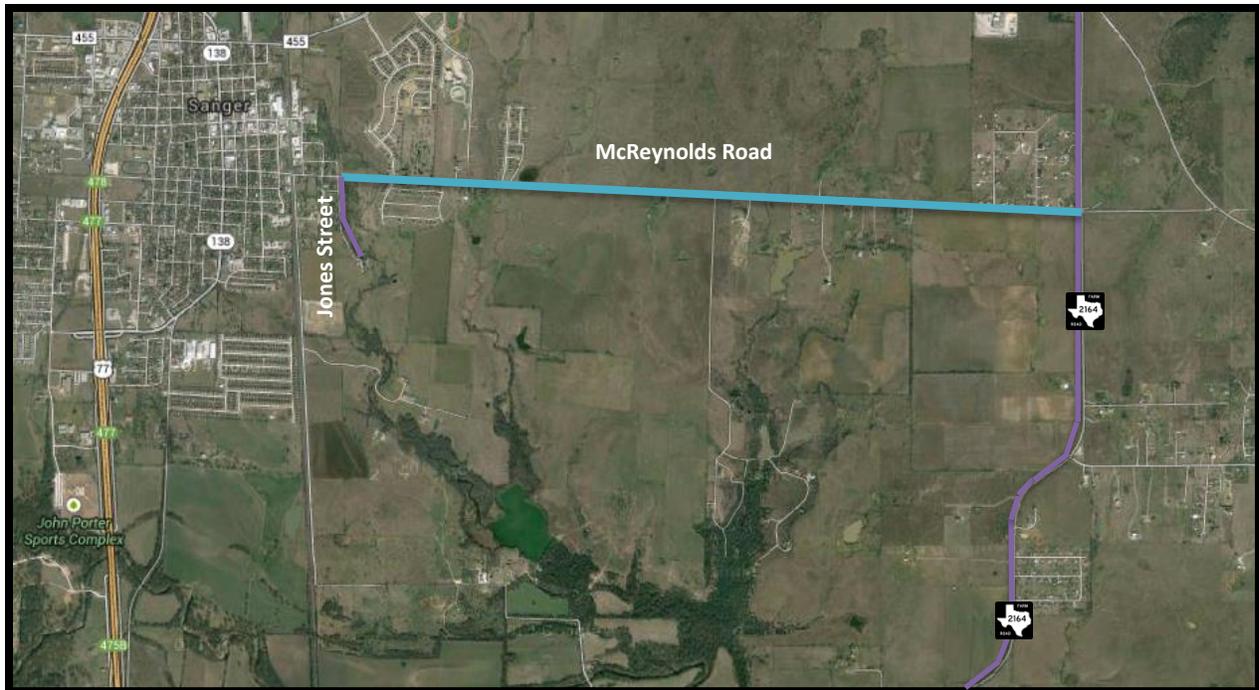


Current Activity:

- **PS&E:** The 100% plans were finalized on January 23, 2015.
- **ROW:** The city is working to acquire easements needed for the project. Sanger retained services of Property Acquisition Services to obtain the necessary easement for the project. One property owner signed easement, leaving one remaining easement. Property owner agreed to a settlement.
- **Construction:** Opened bids on July 26, 2016. It is expected that the project will be awarded, and the contractor will begin work in the fall.
- **ICA:** City council approved ICA amendment with the county. ICA amendment was approved by Denton County Commissioners Court on September 6, 2016.

Naylor Road

Limits (From):	US 380 South	Design Complete:	December 2015
(To):	Martop Road	ROW Acquisition Complete:	May 2016
Est. Const. Cost:	\$3,400,000	Utility Relocations Complete:	September 2016
Project Description:	Design and construct drainage and paving improvements to the roadway	Award Construction Contract:	March 2016
Firm:	Cross Roads, TX	Construction Start:	May 2016
Key Contact:	Jason Pool	Construction Complete:	December 2016

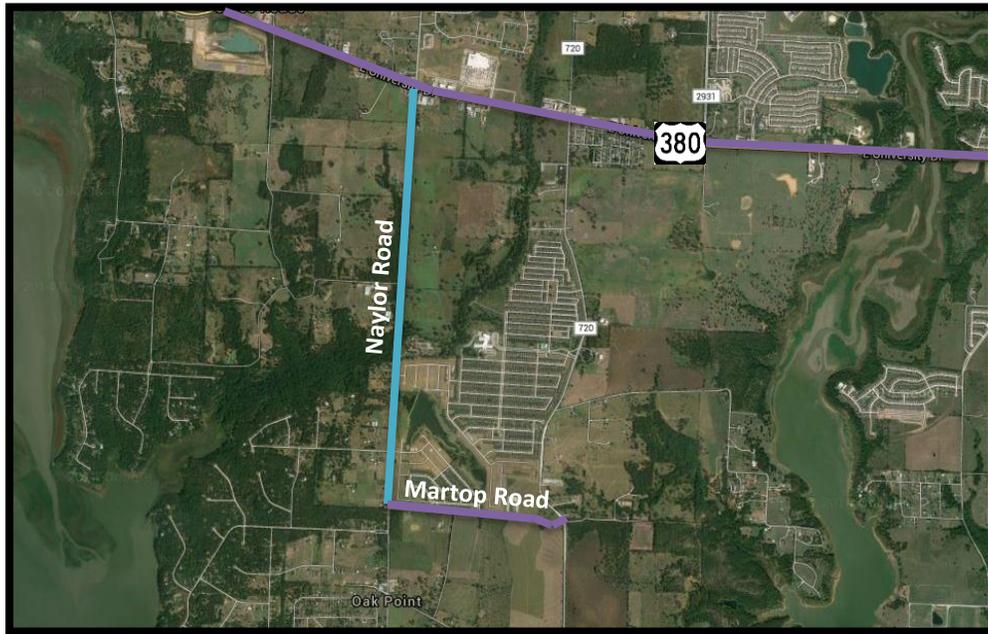

Current Activity:

- **Engineering:** The 100% plans were submitted to the city in December 2015.
- **ROW:** Complete.
- **Utilities:** County/DISD fiber relocations are complete. North Mustang Water line is complete. South Mustang line is designed and awaiting release for construction. AT&T has plans to relocate 11 phone lines on the line on the east side of Naylor; AT&T is clear on east side. New CoServ gas line to be released into Cross Roads portion of the corridor.
- **Construction:** Estimate of construction timeframe from the design engineer is eight months. Project bid on March 11, 2016. Quality Excavation was approved as the contractor by city council on March 21, 2016. Pre-construction meeting was held on May 23, 2016, and notice to proceed was given same day. Current construction activities include: storm crossings have been installed, and cement stabilization has begun on portions of the new pavement area.

Doe Creek Road, Little Elm

Limits:	From US 380 to Rockhill Parkway
Description:	Expand existing 18-foot gravel road to 27-foot concrete roadway with drainage
Construction Cost:	\$1,971,385.48
Firm:	Little Elm
Key Contact:	Jason Laumer, Kimberly Brawner
Project Completion:	September 2016



Current Activity:

- **Construction:** Construction is approximately 98% complete. The roadway is now open to traffic. The only remaining work is striping, reestablishing vegetation, and installing traffic control devices.

Regional Transportation Council

- There were no items to discuss from the August RTC meeting.
